




CITY OF MENLO PARK

Not all projects are listed, for more information please reach out to Menlo Park Public Works (Publicworks@menlopark.gov, (650) 330-6740) for more information. **To return to the map please click on the project number on the left column of the following pages**

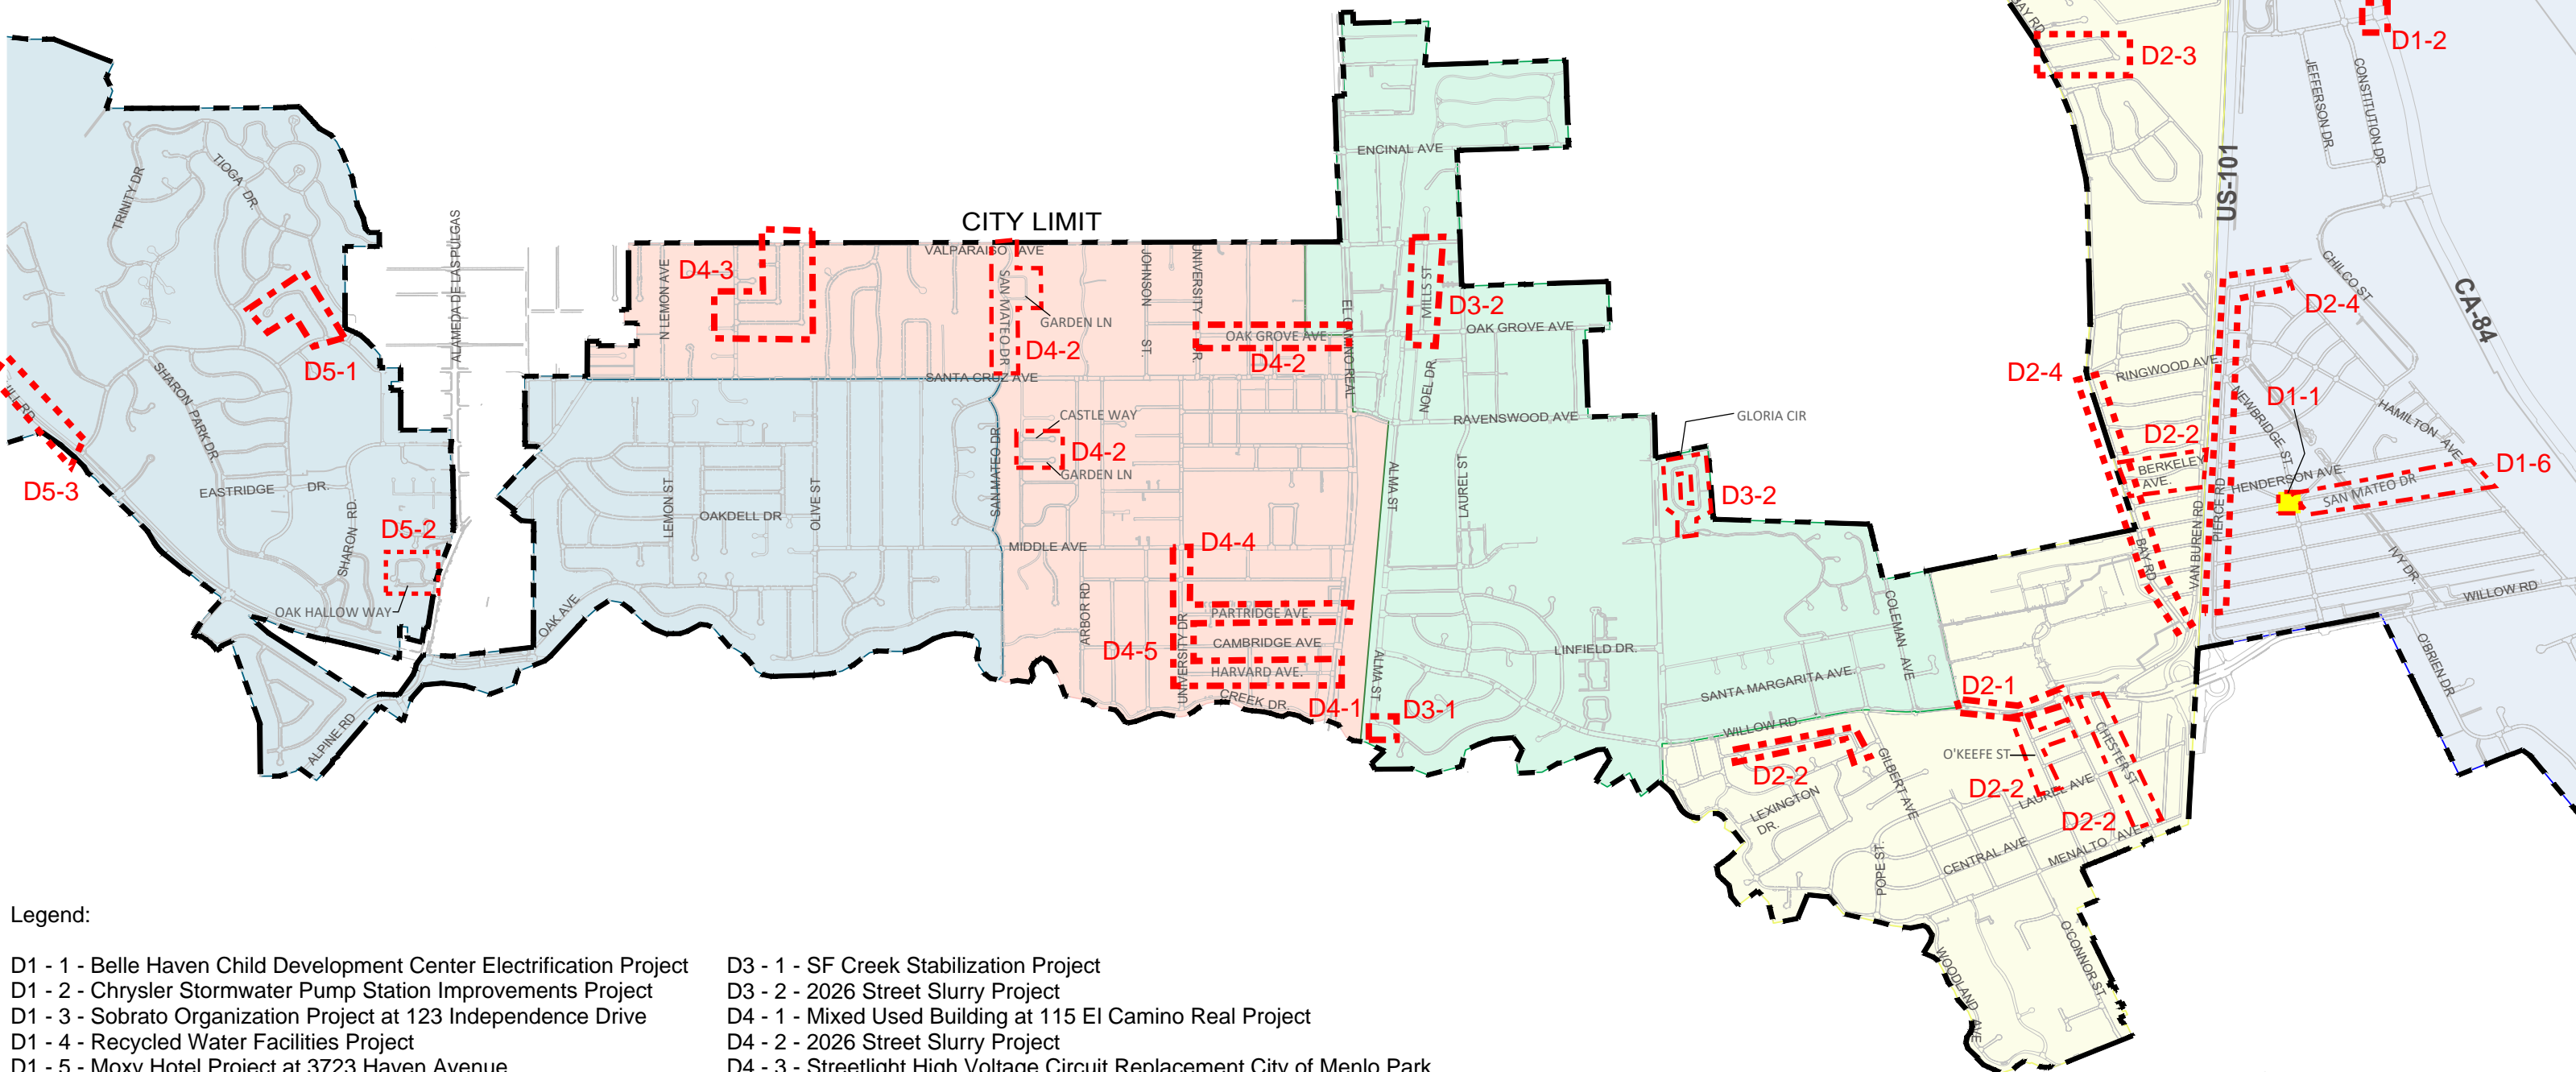

Legend:

- D1 - 1 - Belle Haven Child Development Center Electrification Project
- D1 - 2 - Chrysler Stormwater Pump Station Improvements Project
- D1 - 3 - Sobrato Organization Project at 123 Independence Drive
- D1 - 4 - Recycled Water Facilities Project
- D1 - 5 - Moxy Hotel Project at 3723 Haven Avenue
- D1 - 6 - 2026 Street Slurry Project
- D2 - 1 - Oak Gardens Veterans Housing Project
- D2 - 2 - 2026 Street Slurry Project
- D2 - 3 - California Water - Peggy Ln/Timohty Ln/ Bay Rd
- D2 - 4 - Bay and Pierce Road Improvement Project

- D3 - 1 - SF Creek Stabilization Project
- D3 - 2 - 2026 Street Slurry Project
- D4 - 1 - Mixed Used Building at 115 El Camino Real Project
- D4 - 2 - 2026 Street Slurry Project
- D4 - 3 - Streetlight High Voltage Circuit Replacement City of Menlo Park
- D4 - 4 - Calwater Main Replacement - University Ave
- D4 - 5 - On-Call Repair Services
- D5 - 1 - AT&T Utility Installation
- D5 - 2 - 2026 Street Slurry Project
- D5 - 3 - Sand Hill Water Main Replacement Project

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-1	<p>Belle Haven Child Development Center Electrification Project:</p> <p>The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.</p>	<p>Contractor to schedule the pavement restoration along frontage.</p> <p>No construction schedule as of this time</p>	<p>Major traffic impacts due to lane closures.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City Of Menlo Park Project Manager: Matt Ocamou (650) 817-5292 Michael Fu (650) 330-6706</p> <p>City Of Menlo Park Project Inspector: Menlo Park Building Inspector</p> <p>Contractor: TBD</p> <p>Start Date: Spring 2026 End Date: Summer 2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-2	<p>Chrysler Stormwater Pump Station Improvements Project:</p> <p>The scope of work consists of furnishing & installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump & motor room, electrical control room, engine-generator room, pumping/electrical equipment & controls, hardscaping, landscaping, etc. to complete the work as per City approved plans & specs,</p>	<p>The contractor is working on the roof structure for the new pump station and finalizing the pump station software. Demolition of the existing pumps will commence once final testing of the new pumps is completed.</p> <p>Project completion anticipated for Summer 2026.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City Of Menlo Park Project Manager: Mitchell Supan (650) 330-6756</p> <p>City Of Menlo Park Project Inspector: Holani Vaka (650) 330 - 6753</p> <p>Contractor: APEC</p> <p>Start Date: May 2023 End Date: Summer 2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-3	<p>Sobrato Organization Project at 123 Independence Drive:</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives. Initial construction phase involves demolition and rough grading.</p>	<p>Contractor to continue monitoring SWPPP and access to/from job site.</p> <p>Contractor is schedule to undertakes joint trench work On-Site.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: Sobrato Organization</p> <p>City Of Menlo Park Project Manager: Edress Rangeen (650) 330-6712 Ebby Sohrabi (650)330-6743</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Sobrato Builders, Inc. Dino Spalding (Superintendent) (650) 695-1069</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-4	<p>Recycle Water Facilities Project</p> <p>The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process) Present stage of work is the micro tunneling crossing Bayfront Expressway.</p> <p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Ebby Sohrabi (650)330-6743 Eric Hinkley (650) 330-6749</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Anderson Pacific</p> <p>Start Date: 10/30/2024 End</p>	<p>Contractor is scheduled to continues micro tunneling operation from jacking pit at Bayfront Park entry (Cargill property) to receiving pit at Independence Drive (City's ROW).</p> <p>Contractor to continues monitor and maintain the installed perimeter fence, traffic control plans, and dewatering system for the project.</p>	<p>Major traffic impact due to road closure at Independence/Constitution Drives starting 4/27 for an estimated 9 weeks duration. Minor traffic impact due to temporary pedestrian path adjustment at Bedwell Bayfront Park entry/exit area.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-5	<p>Moxy Hotel Project at 3723 Haven Avenue:</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, fencing, etc. on property. Initial construction phase involves demolition and rough grading.</p>	<p>Contractor to continue monitoring SWPPP and access to/from job site along Haven Avenue frontage. Contractor is schedule to undertakes the installation of dewatering system On-site.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>City Of Menlo Park Project Manager: Jason Santos (650) 330-6715 Rambod Hakhamaneshi (650) 330-6759</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: VCC USA Chris Martorana (Sr. Superintendent) (626) 392-3621</p>		

Menlo Park Construction News Update

June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-6 D2-2 D3-2 D4-2 D5-2	<p>2026 Street Slurry Project</p> <p>The Project includes the base bid and bid alternate streets totaling 3.2 miles to maintain the City's overall PCI in good condition upon completion. The work generally includes: asphalt patching, crack sealing, and tree root remediation; slurry seal for base bid streets; grind (asphalt mill) and overlay for bid alternate streets; minor concrete work (e.g. broken gutter repairs and curb ramps at select locations); signing and striping; high visibility crosswalks for intersections located near schools; replacement of existing speed humps; and red curbs at select intersections per California's Daylighting Law (Assembly Bill 413).</p> <p>Owner: City of Menlo Park</p> <p>City of Menlo Park Project Manager: Andrea Mosqueda (650) 330 -6735</p> <p>City of Menlo Park Project Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: VSS International</p> <p>Start Date: Spring 2026 End Date: Summer 2026</p>	<p>Preliminary signing and striping will continue with permanent signing and striping installation taking place 5/26 - 6/5 and should be finalized by Friday 06/12. Dig out on Amber Way is set to be complete on 6/4.</p> <p>Streets to receive slurry: -Windermere Avenue -Chester Street -McKendry Drive -O'Keefe Street -Gloria Circle -Mills Street -Oak Grove Avenue -San Mateo Drive -Garden Lane -Oak Hollow Way -Castle Way -Saxon Way -Berkeley Avenue</p> <p>Streets to receive grind and overlay: -Mills Court -Poppy Avenue -Magnolia Street</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-1	<p>Oak Gardens Veterans Housing Project:</p> <p>The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.</p> <p>Owner: United State of America Department of Veterans Affairs (VA)</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: Guzman Construction Group (669) 224-9000</p> <p>Start Date:12/12/2024 End Date: 02/02/2026</p>	<p>Contractor is scheduled to continue on-site building construction and off-site material deliveries using Willow Road.</p> <p>Contractor is scheduled to undertakes punch list items for off-site improvements along Willow Road frontage (slurry sealing, stripping and landscape) prior to building occupancy.</p>	<p>Minor traffic impact due to lane closure/adjustment during operation along Willow Road.</p> <p>Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-3	<p>California Water Service - Water Main Replacement on Peggy Ln, Timothy Ln, and Bay Rd</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Timothy Lane, Peggy Lane, and Bay Rd. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Work concurrently on hold, until permits from separate agency are approved. The next phase will include tying in connections along the main water line followed by installation from main water line to laterals for residents.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: California Water Service</p> <p>Cal Water Service Project Manager Mark Trujillo (650) 854-5454</p> <p>City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Construction John Healy (408)371-5510</p>		

Menlo Park Construction News Update

June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-4	<p>Bay and Pierce Road Improvement Project:</p> <p>The base bid spans Bay and Pierce Roads and generally includes installation of slurry seal, asphalt resurfacing, drainage gutters, speed humps, signing and striping, and curb ramps per the Americans with Disabilities Act (ADA). The bid alternate includes intersection improvements at Sharon Road and Eastridge Avenue and Oak Avenue and Oak Knoll Lane. The bid alternate scope of work generally includes new curb extensions, ramps, gutters, sidewalks, rapid flashing beacons, and signing and striping at Safe Routes to School intersections</p>	<p>For the incoming week the following activities will occur:</p> <p>Pierce Rd between Carlton Ave. and Newbridge Ave.- dig out repairs and installation of speed humps</p> <p>Del Norte Ave. between Pierce Rd and Terminal Ave. - dig out repairs and installation of speed humps.</p> <p>Bay Rd from Ringwood Ave. to Van Buren Ave. -reconstruction of curb ramps</p>	<p>Please anticipate minor traffic impacts. There will be partial street closure. (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City of Menlo Park Project Manager: Mitchell Supan (650) 330-6756</p> <p>City of Menlo Park Project Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: Radius Construction</p> <p>Start Date: Summer 2026 End Date: Summer 2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-1	<p>San Francisquito Creek Bank Stabilization Project</p> <p>The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season</p>	<p>Caltrain is planning to begin construction in the SF Creek on June 15 and is anticipated to complete construction in Fall 2026.</p>	<p>Minor traffic impact due to lane closure/adjustment during operation along Willow Road.</p> <p>Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p>Owner: Peninsula Corridor Joint Powers Board</p> <p>City Project Engineer: Mitchell Supan (650)330-6756</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Caltrans</p> <p>Start Date: Spring 2026 End Date: February 2027</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-1	<p>Mixed Used Building at 115 El Camino Real Project</p> <p>This project consists of building a Mixed Used structure at the corner of El Camino Real and Harvard Avenue.</p>	<p>Contractor is scheduled to continue on-site construction.</p> <p>Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter).</p> <p>Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue.</p>	<p>Occasional minor traffic disturbances due to hauling, handling and material deliveries.</p> <p>Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p>City Project Engineer: Rambod Hakhamaneshi (650) 330-6759</p> <p>City Engineering Inspector: Wilson Radford (650) 330-6742</p> <p>Contractor: Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077</p> <p>Start Date: 03/04/2020 End Date: 12/15/2025</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-3	<p>Streetlight High Voltage Circuit Replacement City of Menlo Park</p> <p>The project generally includes replacing existing high voltage electrical circuits with new conduits, conductors, and pull-boxes in the West Menlo neighborhood. The project will also replace existing luminaries with energy efficient LED luminaires and install new street poles and fixtures at select locations. Please refer to the project webpage for additional information including a map detailing proposed street location.</p>	<p>Contractor is scheduled to install light fixtures in the middle of July.</p> <p>After electrical will be installed through conduits to finalize installation</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: City of Menlo Park City of Menlo Park Project</p> <p>City of Menlo Park Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Bay Area Lightworks</p> <p>Start Date: 10/13/2025 End Date: 07/31/2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-4	<p>California Water Service - Water Main Replacement on University Ave, Harvard Ave, and Partridge Ave</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along University Avenue, Harvard Avenue, and Partridge Ave. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Phase 1 work has started on Harvard Avenue.</p> <p>Work includes excavation, main replacement, backfill, and temporary restoration. Fire hydrants will also be replaced.</p> <p>Work on Partridge Avenue anticipated to begin on 6/22</p>	<p>Please anticipate traffic impacts including full street closures and partial lane closures during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: United State of America Department of Veterans Affairs (VA)</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: Guzman Construction Group (669) 224-9000</p> <p>Start Date:12/12/2024 End Date: 02/02/2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-5	<p>Citywide Asphalt And Concrete On-Call Repair Services Project:</p> <p>In general, the project consists of installing concrete sidewalks, curb and gutter, valley gutter, accessible curb ramps, driveways, and asphalt base repairs or overlays in the public right of way.</p>	<p>Digout and root repair work will be taking place along Cambridge Ave on 6/24. Work is expected to be completed within the day.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: City of Menlo Park</p> <p>City Project Engineer: Mitchell Supan (650) 330-6756</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Catos General Engineering (510) 397-2677</p> <p>Start Date: 12/12/2024 End Date: 02/02/2026</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-1	<p>AT&T Project along Deanna Drive.</p> <p>Work includes the installation of interduct telecommunications cables along Deanne Drive by means of open trenching, horizontal boring vis pits, restoration works along Deanne Drive fronting Lots nos.1005, 1055, 1045, 1035, 1025, 1075, 1060, 1095, 1130 in the public right of way.</p>	<p>Contractor is expected to undertake asphalt pavement restoration on affected areas at installed interduct communication cables along Deanna Dr and Avy Avenue weather permit.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 9AM – 3PM) unless otherwise noted.</p> <p>The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, and flaggers as required) at all times during operations.</p>
	<p>Owner: AT&T</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Haleigh Boss (408) 442-2712 Juan (650) 464-9908</p>		

Menlo Park Construction News Update June 17, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-3	<p>Sand Hill Watermain Replacement Project:</p> <p>This project includes abandoning existing 12" to 16" asbestos concrete water mains (ACP) and installing new 12" and 16" high density polyethylene (HDPE) water mains, valves, and appurtenances. The project also includes pavement rehabilitation (with slurry seal and mill and overlay) and signing and striping. The scope includes all other appurtenances and incidentals necessary to complete the work, appendices, and as specified in the special provisions.</p>	<p>Contractor is schedule to continue the required submittals for materials, notification, layout and site preparation recordation prior to mobilization.</p> <p>Contractor is scheduled to undertakes potholing operation to verify existing utility along Monte Rosa (beginning Syskiyou), Sand Hill Road until Sand Hill Circle.</p>	<p>Major traffic impact due to road and/or lane closures along Sand Hill Drive, Monte Rosa and Sand Hill Circle.</p> <p>Approved working hours of 9PM to 6AM. Contractor shall provide traffic control approved by the City and Caltrans as needed.</p>
	<p>City Of Menlo Park Project Manager: Scott Jaw (650) 330-6694</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485 Phillip Leonardo</p> <p>Contractor: Cratus, Inc. Donall Dowd/Project Manager (415) 529-0222</p>		
