




CITY OF MENLO PARK

Not all projects are listed, for more information please reach out to Menlo Park Public Works (Publicworks@menlopark.gov, (650) 330-6740) for more information. **To return to the map please click on the project number on the left column of the following pages**

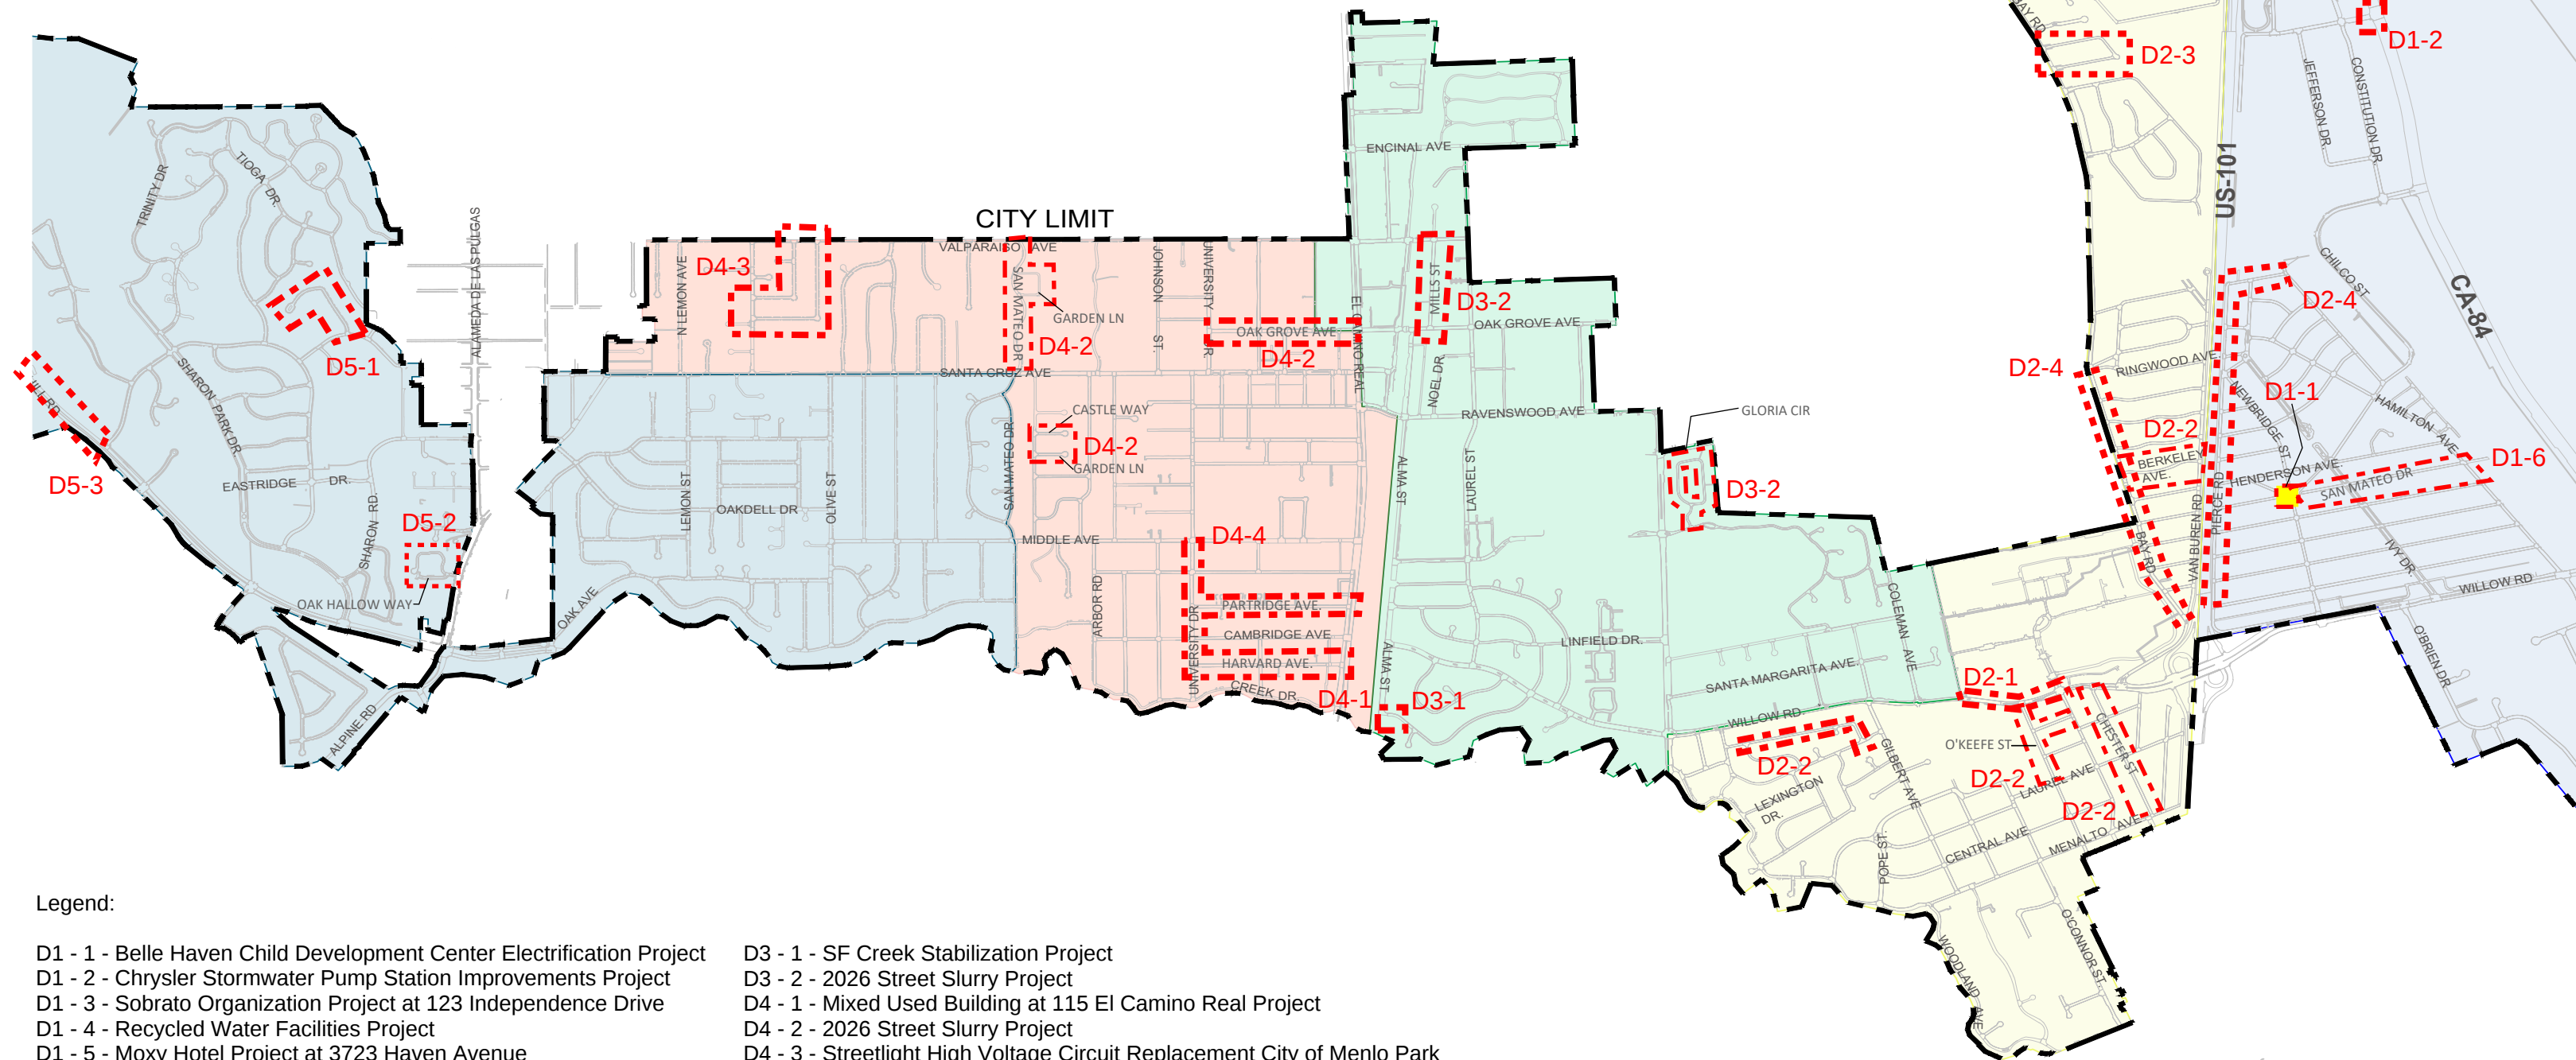

Legend:

D1 - 1 - Belle Haven Child Development Center Electrification Project
D1 - 2 - Chrysler Stormwater Pump Station Improvements Project
D1 - 3 - Sobrato Organization Project at 123 Independence Drive
D1 - 4 - Recycled Water Facilities Project
D1 - 5 - Moxy Hotel Project at 3723 Haven Avenue
D1 - 6 - 2026 Street Slurry Project
D2 - 1 - Oak Gardens Veterans Housing Project
D2 - 2 - 2026 Street Slurry Project
D2 - 3 - California Water - Peggy Ln/Timohty Ln/ Bay Rd
D2 - 4 - Bay and Pierce Road Improvement Project

D3 - 1 - SF Creek Stabilization Project
D3 - 2 - 2026 Street Slurry Project
D4 - 1 - Mixed Used Building at 115 El Camino Real Project
D4 - 2 - 2026 Street Slurry Project
D4 - 3 - Streetlight High Voltage Circuit Replacement City of Menlo Park
D4 - 4 - Calwater Main Replacement - University Ave
D5 - 1 - AT&T Utility Installation
D5 - 2 - 2026 Street Slurry Project
D5 - 3 - Sand Hill Water Main Replacement Project

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-1	Belle Haven Child Development Center Electrification Project: The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.	Contractor to schedule the pavement restoration along frontage. No construction schedule as of this time	Major traffic impacts due to lane closures. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, and flaggers as required) at all times during construction.
	Owner: City of Menlo Park City Of Menlo Park Project Manager: Matt Ocamou (650) 817-5292 Michael Fu (650) 330-6706 City Of Menlo Park Project Inspector: Menlo Park Building Inspector Contractor: TBD Start Date: Spring 2026 End Date: Summer 2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-2	Chrysler Stormwater Pump Station Improvements Project: The scope of work consists of furnishing & installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump & motor room, electrical control room, engine-generator room, pumping/electrical equipment & controls, hardscaping, landscaping, etc. to complete the work as per City approved plans & specs,	Demolition of the existing pumps is underway. The new pumps are operational and commissioning has begun. Installations of the manholes to connect to the underground water retention structure is underway. Project completion anticipated for Fall 2026.	Minor traffic impact expected during operation – truck/equipment exit/entering the site. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	Owner: City of Menlo Park City Of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Of Menlo Park Project Inspector: Holani Vaka (650) 330 - 6753 Contractor: APEC Start Date: May 2023 End Date: Summer 2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-3	Sobrato Organization Project at 123 Independence Drive: This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives. Initial construction phase involves demolition and rough grading.	Contractor to continue monitoring SWPPP and access to/from job site. Permit issued for new joint trench on Chrysler Drive serving 150 Constitution Drive.	Minor traffic impact expected during operation – truck/equipment exit/entering the site. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	Owner: Sobrato Organization City Of Menlo Park Project Manager: Edress Rangeen (650) 330-6712 Ebby Sohrabi (650)330-6743 City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485 Contractor: Sobrato Builders, Inc. Dino Spalding (Superintendent) (650) 695-1069		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-4	Recycle Water Facilities Project The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process) Present stage of work is the micro tunneling crossing Bayfront Expressway.	Contractor to continues monitor and maintain the installed perimeter fence, traffic control plans, and dewatering system for the project at Bayfront Park entry (Cargill property).	Minor traffic impact due to temporary pedestrian path adjustment at Bedwell Bayfront Park entry/exit area. Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.
	Owner: West Bay Sanitary District WBSD Inspector: George Sanchez (650) 477-6425 City of Menlo Park Project Manager (per issued encroachment permit): Ebby Sohrabi (650)330-6743 Eric Hinkley (650) 330-6749 City of Menlo Park Inspector: Mel Yambao (925) 980-7485 Contractor: Anderson Pacific Start Date: 10/30/2024 End		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-5	Moxy Hotel Project at 3723 Haven Avenue: This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, fencing, etc. on property. Initial construction phase involves demolition and rough grading.	Contractor to continue monitoring SWPPP and access to/from job site along Haven Avenue frontage. City and Caltrans issued encroachment permit for the use of crane for the project.	Minor traffic impact expected during operation – truck/equipment exit/entering the site. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	City Of Menlo Park Project Manager: Jason Santos (650) 330-6715 Rambod Hakhamaneshi (650) 330-6759 City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485 Contractor: VCC USA Chris Martorana (Sr. Superintendent) (626) 392-3621		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-6 D2-2 D3-2 D4-2 D5-2	2026 Street Slurry Project The Project includes the base bid and bid alternate streets totaling 3.2 miles to maintain the City's overall PCI in good condition upon completion. The work generally includes: asphalt patching, crack sealing, and tree root remediation; slurry seal for base bid streets; grind (asphalt mill) and overlay for bid alternate streets; minor concrete work (e.g. broken gutter repairs and curb ramps at select locations); signing and striping; high visibility crosswalks for intersections located near schools; replacement of existing speed humps; and red curbs at select intersections per California's Daylighting Law (Assembly Bill 413).	The project, which included slurry, grind and overlay, and signing and striping, has been substantially completed. The contractor is currently finalizing punch-list items before the project is fully completed.	Minor traffic impact expected during operation – truck/equipment exit/entering the site. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	Owner: City of Menlo Park		
	City of Menlo Park Project Manager: Andrea Mosqueda (650) 330 -6735		
	City of Menlo Park Project Inspector: Holani Vaka (650)330-6753		
	Contractor: VSS International Start Date: Spring 2026 End Date: Summer 2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-1	Oak Gardens Veterans Housing Project: The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.	Roadway restoration work has been completed. City awaits final on-site items to be completed before full project completion and closeout.	Minor traffic impact due to lane closure/adjustment during operation along Willow Road. Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.
	Owner: United State of America Department of Veterans Affairs (VA) City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Guzman Construction Group (669) 224-9000 Start Date: 12/12/2024 End Date: 02/02/2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-3	California Water Service - Water Main Replacement on Peggy Ln, Timothy Ln, and Bay Rd The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Timothy Lane, Peggy Lane, and Bay Rd. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.	Work concurrently on hold, until permits from separate agency are approved. The next phase will include tying in connections along the main water line followed by installation from main water line to laterals for residents.	Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations
	Owner: California Water Service Cal Water Service Project Manager Mark Trujillo (650) 854-5454 City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: West Valley Construction John Healy (408)371-5510		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-4	Bay and Pierce Road Improvement Project: The base bid spans Bay and Pierce Roads and generally includes installation of slurry seal, asphalt resurfacing, drainage gutters, speed humps, signing and striping, and curb ramps per the Americans with Disabilities Act (ADA). The bid alternate includes intersection improvements at Sharon Road and Eastridge Avenue and Oak Avenue and Oak Knoll Lane. The bid alternate scope of work generally includes new curb extensions, ramps, gutters, sidewalks, rapid flashing beacons, and signing and striping at Safe Routes to School intersections	This week and the week of August 10th construction will be focused on the following: - Striping of Pierce Rd, Del Norte, Bay Rd and Sharon Rd/Eastridge Ave, and Oak Ave. and Oak Knoll intersections, - Installation of traffic signs, - Repair of a defective ADA ramp on Oak Ave. - Installation of rectangular rapid flashing beacon at the intersection of Sharon Rd/Eastridge Ave.	Please anticipate traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	Owner: City of Menlo Park City of Menlo Park Project Manager: Rene Punsalan (650)330-6794 City of Menlo Park Project Inspector: Holani Vaka (650)330-6753 Contractor: Radius Construction Start Date: Summer 2026 End Date: Summer 2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-1	San Francisquito Creek Bank Stabilization Project The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season	Caltrain began construction in the SF Creek on June 15. Currently, the contractor is shoring and importing boulder bedding for the creek. Construction is anticipated to be completed in Fall 2026.	Minor traffic impact due to lane closure/adjustment during operation along Willow Road. Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.
	Owner: Peninsula Corridor Joint Powers Board City Project Engineer: Mitchell Supan (650)330-6756 City Engineering Inspector: Holani Vaka (650) 330-6753 Contractor: Caltrans Start Date: Spring 2026 End Date: February 2027		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-1	Mixed Used Building at 115 El Camino Real Project This project consists of building a Mixed Used structure at the corner of El Camino Real and Harvard Avenue.	Contractor is scheduled to continue on-site construction. Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter). Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue.	Occasional minor traffic disturbances due to hauling, handling and material deliveries. Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.
	City Project Engineer: Rambod Hakhamaneshi (650) 330-6759 City Engineering Inspector: Wilson Radford (650) 330-6742 Contractor: Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077 Start Date: 03/04/2020 End Date: 12/15/2025		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-3	Streetlight High Voltage Circuit Replacement City of Menlo Park The project generally includes replacing existing high voltage electrical circuits with new conduits, conductors, and pull-boxes in the West Menlo neighborhood. The project will also replace existing luminaries with energy efficient LED luminaires and install new street poles and fixtures at select locations. Please refer to the project webpage for additional information including a map detailing proposed street location.	Contractor is scheduled to install street light pole, wire, and light fixtures in the middle of August. The project is scheduled to complete at the end of 2026.	Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations
	Owner: City of Menlo Park City of Menlo Park Project City of Menlo Park Inspector: Holani Vaka (650) 330-6753 Contractor: Bay Area Lightworks Start Date: 10/13/2025 End Date: 12/31/2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-4	California Water Service - Water Main Replacement on University Ave, Harvard Ave, and Partridge Ave The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along University Avenue, Harvard Avenue, and Partridge Ave. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.	Installation of hydrants along University Avenue. Services along Harvard Avenue and Partridge Avenue Restoration is scheduled after all water main work has been completed. Coordination with the City on water main work is continuous. Schedule adjustments are being communicated closely.	Please anticipate traffic impacts including partial lane closures and full road closures during construction activity (typically 8AM – 5PM) unless otherwise noted. The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	Owner: United State of America Department of Veterans Affairs (VA) City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Guzman Construction Group (669) 224-9000 Start Date: 12/12/2024 End Date: 02/02/2026		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-1	AT&T Project along Deanna Drive. Work includes the installation of interduct telecommunications cables along Deanne Drive by means of open trenching, horizontal boring vis pits, restoration works along Deanne Drive fronting Lots nos.1005, 1055, 1045, 1035, 1025, 1075, 1060, 1095, 1130 in the public right of way.	Contractor is expected to undertake asphalt pavement restoration on affected areas at installed interduct communication cables along Deanna Dr and Avy Avenue weather permit.	Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 9AM – 3PM) unless otherwise noted. The contractor shall adhere to City- approved traffic control plans (including implementation of temporary signs, cones, and flaggers as required) at all times during operations.
	Owner: AT&T City Engineering Inspector: Wil Radford (650)330-6742 Contractor: West Valley Haleigh Boss (408) 442-2712 Juan (650) 464-9908		

Menlo Park Construction News Update

August 5, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-3	Sand Hill Watermain Replacement Project: This project includes abandoning existing 12" to 16" asbestos concrete water mains (ACP) and installing new 12" and 16" high density polyethylene (HDPE) water mains, valves, and appurtenances. The project also includes pavement rehabilitation (with slurry seal and mill and overlay) and signing and striping. The scope includes all other appurtenances and incidentals necessary to complete the work, appendices, and as specified in the special provisions.	Construction Schedule: Water main installation along Sand Hill Road is scheduled to continue until 8/2. This work will take place during the evening from 9PM to 6AM.	Major traffic impact due to road and/or lane closures along Sand Hill Drive, Monte Rosa and Sand Hill Circle. Approved working hours of 8AM to 5PM daywork and 9PM to 6AM nightwork. Contractor shall provide traffic control approved by the City and Caltrans as needed.
	City Of Menlo Park Project Manager: Scott Jaw (650) 330-6694 City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485 Contractor: Cratus, Inc. Donall Dowd/Project Manager (415) 529-0222		
