




# CITY OF MENLO PARK

Not all projects are listed, for more information please reach out to Menlo Park Public Works (Publicworks@menlopark.gov, (650) 330-6740) for more information. **To return to the map please click on the project number on the left column of the following pages**

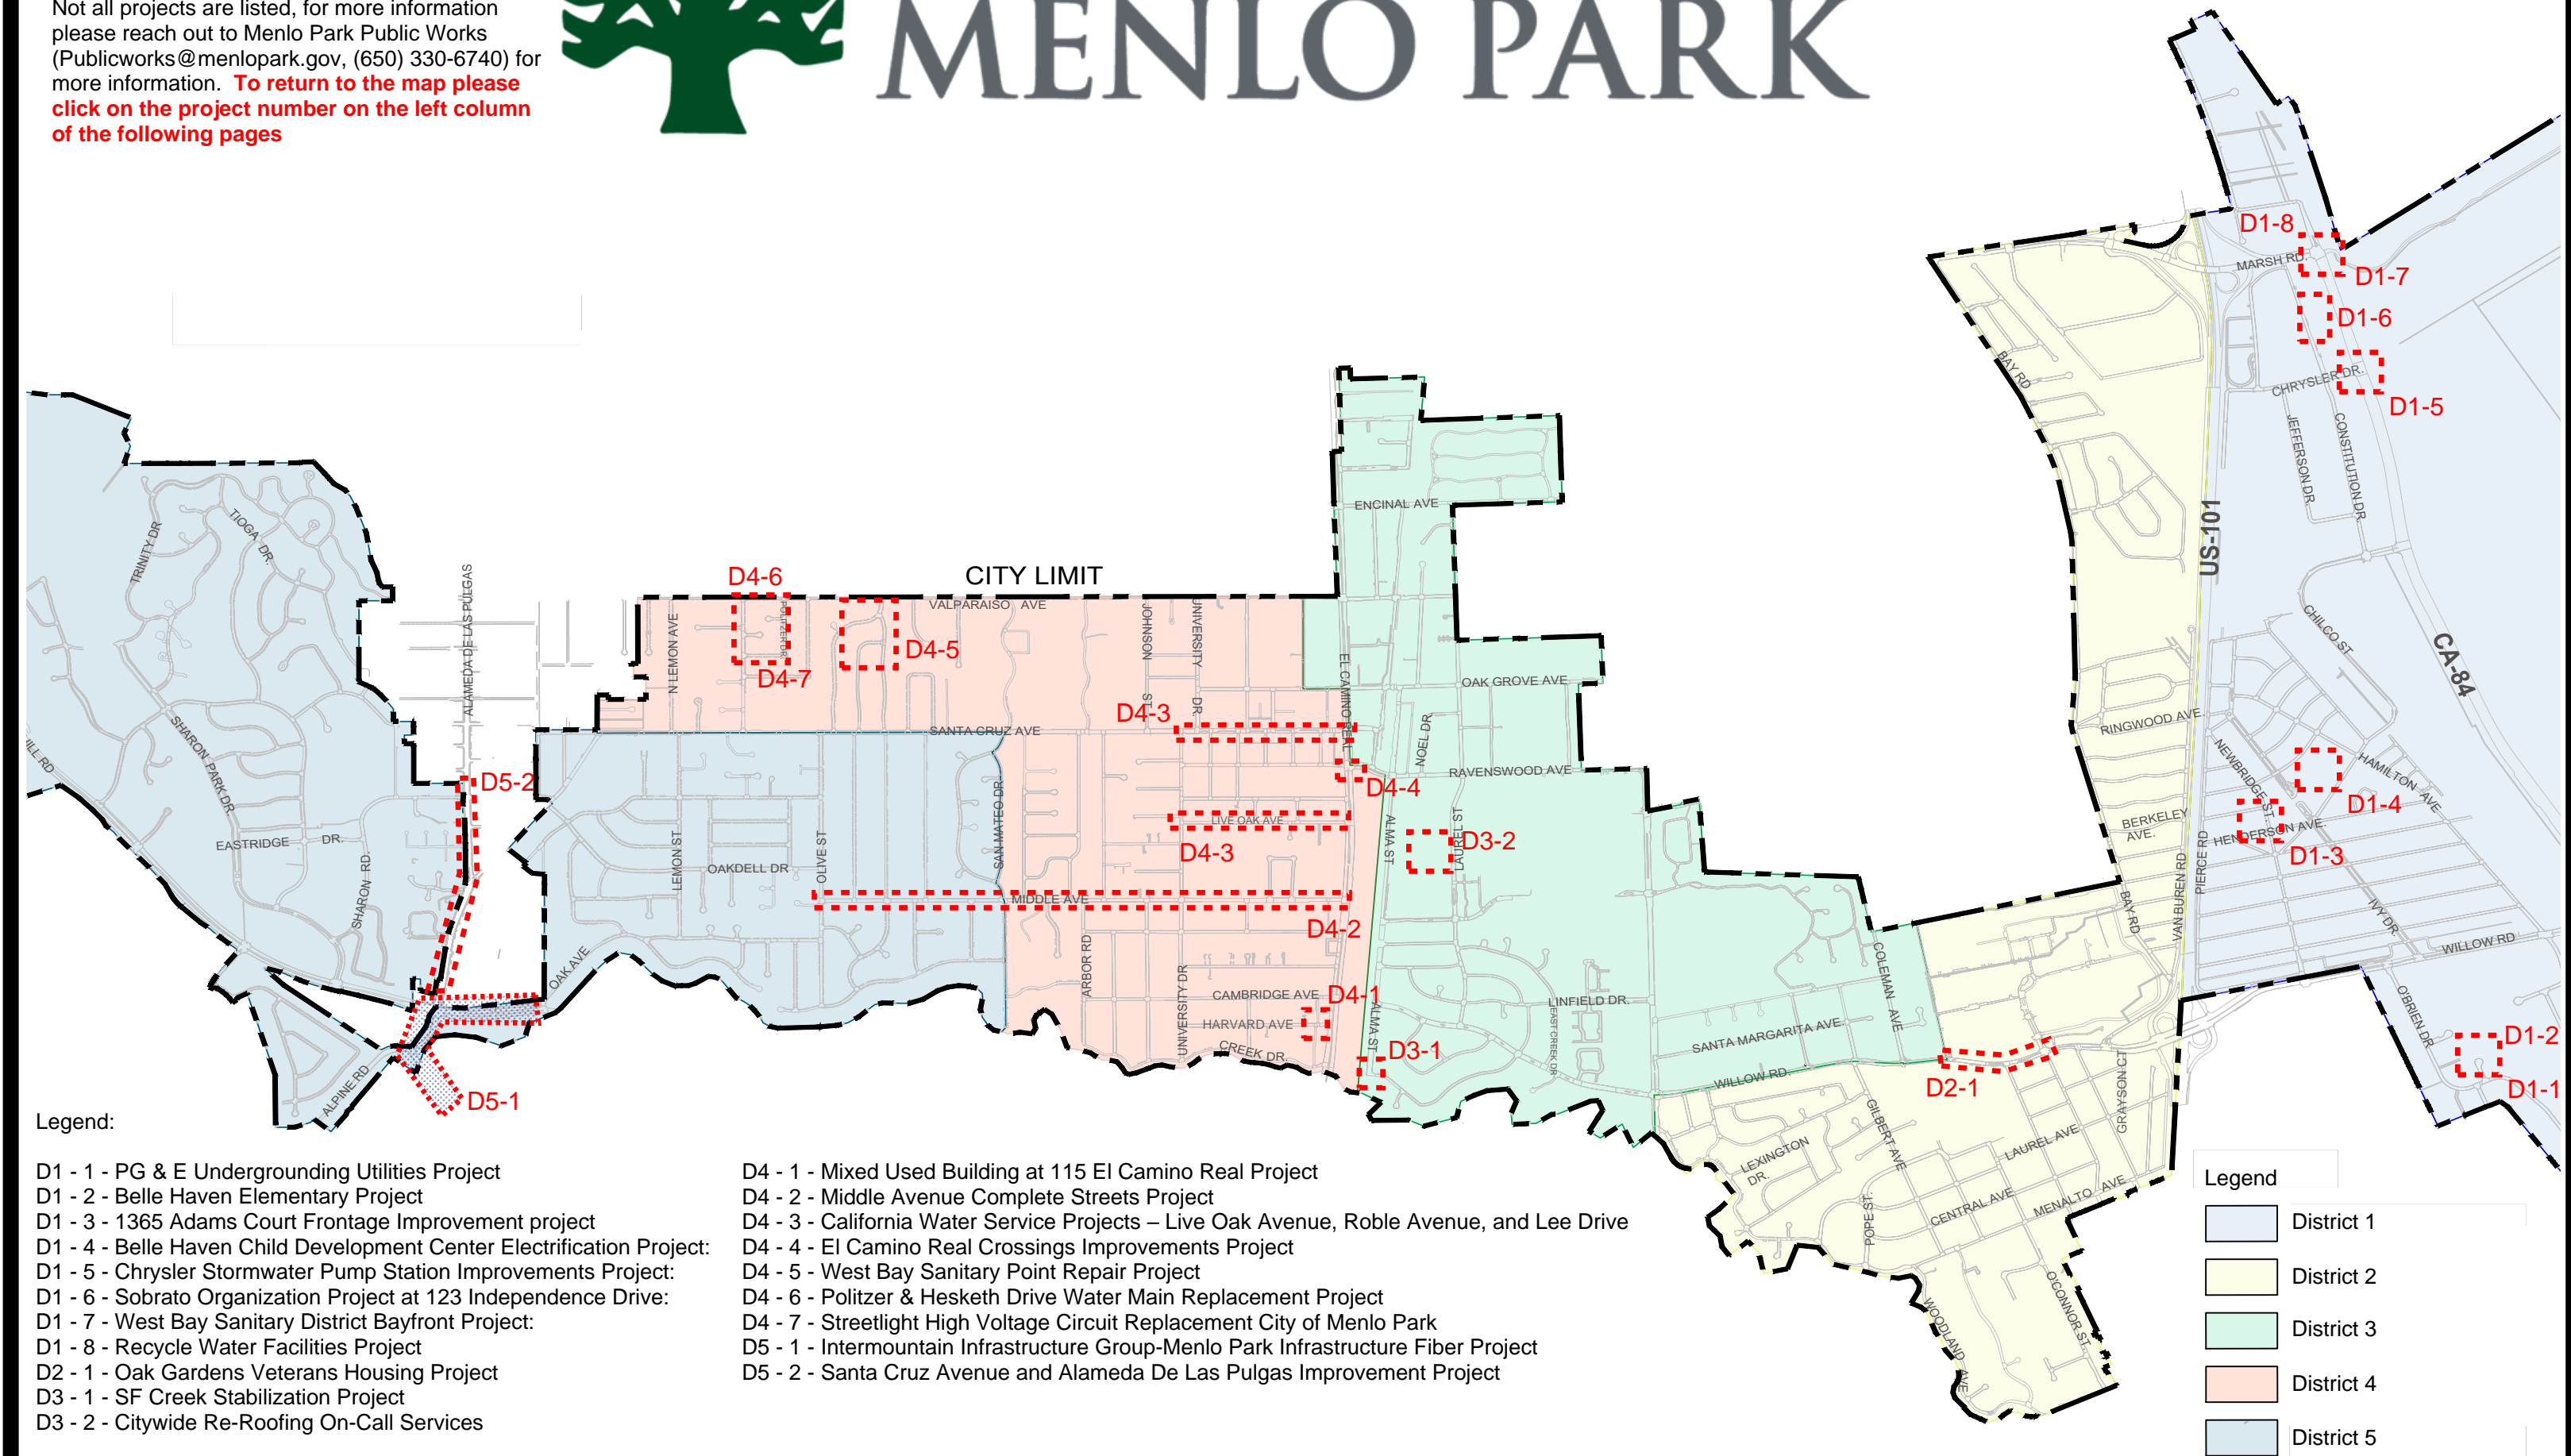

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-1	<b>PG &amp; E Undergrounding Utilities Project</b>  The project is located at 1180 O'Brien Drive and involves the installation of electric transformer, service vault, main switchboard, and undergrounding service/primary from across PG&E pole along O'Brien Drive per issued encroachment permits.	No construction schedule as of this time.	No traffic impacts.  The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations
	<b>Owner:</b> SBK Obrien LLC  <b>City of Menlo Park Project Manager (per issued encroachment permit):</b> Eric Hinkley (650) 330-6749 Wilson Radford (650) 330-6742  <b>City of Menlo Park Inspector:</b> Mel Yambao (925) 980-7485  <b>Contractor:</b> ANZA Engineering		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-2	<p><b>Belle Haven Elementary Project</b></p> <p>The project is located at 415 Ivy Drive and involves the installation of concrete driveways, sidewalk, curb, &amp; gutter along Chilco and Almanor Streets (City's ROW).</p>	No construction schedule as of this time.	<p>Please anticipate traffic impacts including lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. Please anticipate traffic impacts including lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. No anticipate traffic impacts.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> Menlo Park School District</p> <p><b>WBSD Inspector:</b> George Sanchez (650) 477-6425</p> <p><b>City of Menlo Park Project Manager (per issued encroachment permit):</b> Wilson Radford (650) 330-6742</p> <p><b>City of Menlo Park Inspector:</b> Mel Yambao (925) 980-7485</p> <p><b>Contractor:</b> Jacob Ciari, Project Engineer (408) 296-6010</p> <p><b>Start Date: 9/15/2025</b> <b>Estimated date of completion: May 2026</b></p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-3	<p><b>1365 Adams Court Frontage Improvement Project</b></p> <p>The works involving concrete ramp/sidewalk, crosswalk, streetlights, irrigation, landscape, stripping &amp; other related improvements along Adams Drive and Adams Court.</p>	Contractor is scheduled to undertakes the installation of streetlight foundation along project frontages.	<p>Major traffic impacts due to lane closures.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> INTERTEK</p> <p><b>City of Menlo Park Project Manager (per issued encroachment permit):</b> Eric Hinkley (650) 330-6749 Wilson Radford (650) 330-6742</p> <p><b>City of Menlo Park Inspector:</b> Mel Yambao (925) 980-7485</p> <p><b>Contractor:</b> Davidovits/Valacad Co. Neal Gregorin General Superintendent (650) 218-1384</p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-4	<p><b>Belle Haven Child Development Center Electrification Project:</b></p> <p>The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.</p>	<p>The City is proceeding with the design phase. We are currently reviewing a Basis of Design document from KPA Group.</p>	<p>Major traffic impact is expected due to lane closure during operation.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> City of Menlo Park</p> <p><b>City Of Menlo Park Project Manager:</b> Matt Oscamou (650) 817-5292 Michael Fu (650) 330-6706</p> <p><b>City Of Menlo Park Project Inspector:</b> Menlo Park Building Inspector</p> <p><b>Contractor:</b> TBD</p> <p><b>Start Date: Spring 2026</b> <b>End Date: Summer 2026</b></p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-5	<p><b>Chrysler Stormwater Pump Station Improvements Project:</b></p> <p>The scope of work consists of furnishing &amp; installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump &amp; motor room, electrical control room, engine- generator room, pumping/electrical equipment &amp; controls, hardscaping, landscaping, etc. to complete the work as per City approved plans &amp; specs,</p>	<p>The contractor is working on the testing of the new pumps. They are estimated to be operational in early November. Demolition of the existing pumps will commence once final testing of the new pumps is completed.</p> <p>Project completion anticipated for February 2026.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> City of Menlo Park</p> <p><b>City Of Menlo Park Project Manager:</b> Mitchell Supan (650) 330-6756</p> <p><b>City Of Menlo Park Project Inspector:</b> Holani Vaka (650) 330 - 6753</p> <p><b>Contractor:</b> APEC</p> <p><b>Start Date: May 2023</b> <b>End Date: November 2025</b></p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-6	<b>Sobrato Organization Project at 123 Independence Drive:</b>  This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives. Initial construction phase involves demolition and rough grading.	Contractor is scheduled to monitor and maintain BMPs/SWPPP on-site and off-site.	Occasional minor traffic impact due to enter/exit along Constitution and Independence Drives.  Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.
	<b>Owner:</b> Sobrato Organization  <b>City Of Menlo Park Project Manager:</b> Edress Rangeen (650) 330-6712 Ebby Sohrabi (650)330-6743  <b>City Of Menlo Park Project Inspector:</b> Mel Yambao (925) 980-7485  <b>Contractor:</b> <b>Sobrato Builders, Inc.</b> Dino Spalding (Superintendent) (650) 695-1069  <b>Start Date: 05/30/2024</b>		



## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-7	<p><b>West Bay Sanitary District Bayfront Project:</b></p> <p>This is the WBSD sanitary sewer main upgrades at Marsh Road and Bayfront Park. Works include replacement of existing sanitary sewer main system, removal and protection of existing improvements, concrete/asphalt paving, signalization upgrades, sign &amp; striping and other related off-site/on-site improvements. Additional and modified works includes the installation of junction structure, 12" piping lines, 54'MH, paving (with replacement of signal traffic loops, and other related restoration works along Caltrans ROW.</p>	Contractor is scheduled to continue the additional work per issued Caltrans permit at Bayfront Park entry/Bayfront Expressway/Marsh/Haven area.	<p>Occasional traffic disturbances due to pedestrian trail closure along Bayfront Expressway.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City and Caltrans.</p>
	<p><b>Owner:</b> West Bay Sanitary District</p> <p><b>WBSD Inspector:</b> George Sanchez (650) 477-6425</p> <p><b>City of Menlo Park Project Manager (per issued encroachment permit):</b> Jason Santos (650) 330-6715</p> <p><b>City of Menlo Park Inspector:</b> Mel Yambao (925) 980-7485</p> <p><b>Contractor:</b> Ranger Construction</p>		



## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-8	<p><b>Recycle Water Facilities Project</b></p> <p>The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process)</p>	Contractor is schedule to mobilize and relocate backflow preventive device in preparation for the placement of jacking boring pit for micro-tunneling at Bedwell Bayfront Park (Cargill property).	<p>Minor traffic impact due to pedestrian path lane adjustment during operation around Bedwell Bayfront Park entry/exit area.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>
	<p><b>Owner:</b> West Bay Sanitary District</p> <p><b>WBSD Inspector:</b> George Sanchez (650) 477-6425</p> <p><b>City of Menlo Park Project Manager (per issued encroachment permit):</b> Ebby Sohrabi (650)330-6743 Eric Hinkley (650) 330-6749</p> <p><b>City of Menlo Park Inspector:</b> Mel Yambao (925) 980-7485</p> <p><b>Contractor:</b> Anderson Pacific</p> <p><b>Start Date: 10/30/2024 End Revised Date: 11/15/2025 per latest Permit extension</b></p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-1	<p><b>Oak Gardens Veterans Housing Project:</b></p> <p>The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.</p>	<p>Contractor is scheduled to continue on-site building construction and off-site material deliveries using Willow Road.</p> <p>Contractor is scheduled to continue site clearing, and installation of on- site and off-site utilities.</p> <p>Schedule of construction is being communicated with the City to obtain accurate updates to the project.</p>	<p>Minor traffic impact due to lane closure/adjustment during operation along Willow Road.</p> <p>Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p><b>Owner:</b> United State of America Department of Veterans Affairs (VA)</p> <p><b>City of Menlo Park Project Manager:</b> Jason Santos (650) 330-6715</p> <p><b>City Engineering Inspector:</b> Wil Radford (650)330-6742</p> <p><b>Contractor:</b> Guzman Construction Group (669) 224-9000</p> <p><b>Start Date:</b>12/12/2024 <b>End Date:</b> 02/02/2026</p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-1	<p><b>San Francisquito Creek Bank Stabilization Project</b></p> <p>The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season</p>	<p>The contractor is collecting federal permits to begin mobilization for the full restoration. Project construction is expected to continue in Spring 2026.</p>	<p>No major traffic impacts are expected at this time.</p>
	<p><b>Owner:</b> Peninsula Corridor Joint Powers Board</p> <p><b>City Project Engineer:</b> Mitchell Supan (650)330-6756</p> <p><b>City Engineering Inspector:</b> Holani Vaka (650) 330-6753</p> <p><b>Contractor:</b> Caltrans</p> <p><b>Start Date: Spring 2026</b></p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-2	<b>Citywide Re-Roofing On-Call Services</b>  The project includes removal and replacement of the existing roof for specified buildings along city hall	The City is working with the contractor on the plan for the next phase of the project. There is no scheduled work at this time.	No major traffic impacts are expected at this time. Some minor pedestrian impacts are expected in areas that will be coned off to the public.
	<b>Owner:</b> City of Menlo Park  <b>City of Menlo Park Project Manager:</b> Mitchell Supan (650) 330-6756  <b>City Engineering Inspector:</b> Menlo Park Building Department  <b>Contractor:</b> San Francisco Roofing Services Inc.  <b>Start Date: August 2024</b> <b>End Date: June 2027</b>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-1	<p><b>Mixed Used Building at 115 El Camino Real Project</b></p> <p>This project consists of building a Mixed Used structure at the corner of El Camino Real and Harvard Avenue.</p>	<p>Contractor is scheduled to continue on-site construction.</p> <p>Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter).</p> <p>Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue..</p>	<p>Occasional minor traffic disturbances due to hauling, handling and material deliveries.</p> <p>Contractors shall provide traffic control approved by City as needed.</p>
	<p><b>City Project Engineer:</b> Rambod Hakhamaneshi (650) 330-6759</p> <p><b>City Engineering Inspector:</b> Wilson Radford (650) 330-6742</p> <p><b>Contractor:</b> Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077</p> <p><b>Start Date: 03/04/2020</b> <b>End Date: 12/15/2025</b></p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-2	<p><b>Middle Avenue Complete Streets Project</b></p> <p>The project will include traffic calming improvements along Middle Avenue from El Camino Real to Olive Street. The scope of work generally consists of new signing and striping (including bicycle lanes), curb ramps, drainage gutters, speed humps, rectangular rapid flashing beacons, and asphalt resurfacing with the project corridor. The project will enhance safety for pedestrians and bicyclists, reduce vehicle speed and improve connectivity to schools, parks, stores, and adjacent neighborhoods.</p>	<p>The contractor has finished foundation work for the project's upcoming rapid flashing beacons and speed feedback signs. Speedfeed back signs are scheduled to be installed next week. The rapid flashing beacons have a long material lead time and staff will provide updates on its installation date as part of this weekly update.</p> <p>To minimize disturbance to school drop-off and pick-up hours, work will take place outside of peak commute hours (between 9AM – 3PM).</p>	<p>Please anticipate traffic impacts including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> California Water Service</p> <p><b>Cal Water Service Project Manager</b> Erik Martin (650) 854-5454</p> <p><b>City of Menlo Park Project Manager:</b> Jason Santos (650) 330-6715</p> <p><b>City Engineering Inspector:</b> Wil Radford (650)330-6742</p> <p><b>Contractor:</b> West Valley Construction John Healy (408)371-5510</p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-3	<p><b>California Water Service – Live Oak Avenue, Roble Avenue, and Lee Drive</b></p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Live Oak Avenue, Roble Avenue, and Lee Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Contractor is beginning to raise underground facilities due to recent completed paving work. Road striping will be scheduled when work is complete.</p> <p>Schedule of construction is being communicated with the City to obtain accurate updates to the project.</p>	<p>Please anticipate traffic impacts including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p><b>Owner:</b> California Water Service</p> <p><b>Cal Water Service Project Manager</b> Erik Martin (650) 854-5454</p> <p><b>City of Menlo Park Project Manager:</b> Jason Santos (650) 330-6715</p> <p><b>City Engineering Inspector:</b> Wil Radford (650)330-6742</p> <p><b>Contractor:</b> West Valley Construction John Healy (408)371-5510</p>		



## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-4	<b>El Camino Real Crossings Improvements Project</b>  The City of Menlo Park's El Camino Real Corridor Study reviewed and recommend potential transportation and safety improvements to El Camino Real, making it safer and more efficient to move along and across El Camino for all modes of travel: pedestrians, bicycles, automobiles, and transit.	Construction is substantially complete pending project closure.	Please anticipate traffic impacts including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.  The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.
	<b>Owner:</b> City of Menlo Park/Caltrans  <b>City of Menlo Park Project Manager:</b> Saeed Shahmirzai (650) 450 - 3507  <b>City Engineering Inspector:</b> Saeed Shahmirzai (650) 450 - 3507  <b>Contractor:</b> Zara Construction Atif Zahoor (650) 353 - 8485  <b>Start Date: 08/25/2025</b> <b>End Date: 10/31/2025</b>	Contractor has begun sewer main replacement work.  The following streets are scheduled to receive replacement mains:	

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-5	<b>West Bay Sanitary Point Repair Project</b>  The scope of work includes trenching to access the existing sewer mains, removal and replacement of existing sewer mains, and the subsequent restoration of all affected surfaces	<ul style="list-style-type: none"> <li>Rosefield Way</li> <li>Cotton Street</li> <li>Hobart Street</li> <li>Hillview Drive</li> <li>Olive Street</li> </ul> Schedule of construction activities is being communicated with the City to obtain accurate updates of the project.	Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.  The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations
	<b>Owner:</b> West Bay Sanitary District  <b>WBSD Inspector</b> George Sanchez (650) 477 - 6425  <b>City of Menlo Park Project Manager:</b> Juvenal Marin Sanchez (650) 330-6741  <b>City Engineering Inspector:</b> Wil Radford (650)330-6742		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-6	<p><b>Politzer &amp; Hesketh Drive Water Main Replacement Project</b></p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Politzer &amp; Hesketh Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Contractor is beginning to raise underground facilities due to recent completed paving work. Road striping will be scheduled when work is complete.</p> <p>Schedule of construction is being communicated with the City to obtain accurate updates to the project.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p><b>Owner:</b> California Water Service</p> <p><b>Cal Water Service Project Manager</b> Andrew Westbrook (650) 334-5920</p> <p><b>City of Menlo Park Project Manager:</b> Juvenal Marin Sanchez (650) 330-6741</p> <p><b>City Engineering Inspector:</b> Wil Radford (650)330-6742</p> <p><b>Contractor:</b> West Valley Construction John Healy (408) 371-5510</p> <p><b>Start Date: 06/18/2025</b> <b>End Date: 11/14/2025</b></p>		

## Menlo Park Construction News Update

### January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-7	<p><b>Streetlight High Voltage Circuit Replacement City of Menlo Park</b></p> <p>The project generally includes replacing existing high voltage electrical circuits with new conduits, conductors, and pull-boxes in the West Menlo neighborhood. The project will also replace existing luminaires with energy efficient LED luminaires and install new street poles and fixtures at select locations. Please refer to the project webpage for additional information including a map detailing proposed street location.</p>	<p>The contractor has completed the underground electrical conduit work at Politzer Dr., and Hillview Dr. Conduit installations at Hobart St. and Cotton St. are scheduled to be completed this coming week. The contractor will restore bore pit potholes and begin connections to light poles after conduit installations are finished at the subject streets.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p><b>Owner:</b> City of Menlo Park City of Menlo Park Project</p> <p><b>Manager:</b> Holani Vaka (650) 330-6753</p> <p><b>City Engineering Inspector:</b> Holani Vaka (650) 330-6753</p> <p><b>Contractor:</b> Bay Area Lightworks</p> <p><b>Start Date:</b> 10/13/2025 <b>End Date:</b> 07/31/2026</p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-1	<b>Intermountain Infrastructure Group-Menlo Park Infrastructure Fiber Project:</b>  Work entails the installation of, via directional boring method, telecommunications conduits along Sand Hill Rd. from the western City Limit into the City of Palo Alto.	Contractor continues work on conduit bridge attachment. Most work is in City of Palo Alto right of way.	No construction traffic delays are expected  Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.
	<b>Owner:</b> Ryan De Long  <b>Intermountain Infrastructure Group, LLC Project Manager</b> Douglas Sink (925) 247-4227  <b>City of Menlo Park Project Manager:</b> Jason Santos (650) 330-6715  <b>City Engineering Inspector:</b> Wil Radford (650)330-6742  <b>Contractor:</b> Solcom (510) 940 - 2490  <b>Start Date: 05/01/2025</b> <b>End Date: 09/05/2025</b>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-2	<p><b>Santa Cruz Avenue and Alameda De Las Pulgas Improvement Project</b>  <b>The project scope includes:</b></p> <p>Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue: Enhance existing sidewalk and bicycle lanes by reducing this section down to one vehicle lane per direction with a two-way center left turn lane.</p> <p>Santa Cruz Avenue from Alameda de las Pulgas to Sand Hill Road: Enhance existing sidewalk and add new bicycle lanes by removing one of the two southbound vehicular lanes.</p>	<p>Contractor continues work on conduit bridge attachment. Most work is in City of Palo Alto right of way.</p> <p>Construction on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue is underway.</p> <p><a href="https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project">https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project</a></p> <p>Construction on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue is underway.</p> <p><a href="https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project">https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project</a></p> <p>No work is scheduled at this time</p>	<p>No construction traffic delays are expected</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.</p>
	<p><b>Owner:</b> San Mateo County</p> <p><b>San Mateo County Project Manager:</b> Leo Chow (650) 399-6415</p> <p><b>City of Menlo Park Project Manager:</b> Rich Angulo (650) 330-6771</p> <p><b>Contractor:</b> RK Engineering Tom Tierney – Project Engineer (415) 420-9993</p> <p><b>Start Date: 03/05/2024</b>  <b>End Date: End of Summer 2025</b></p>		

## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
1	<p><b>Citywide Asphalt And Concrete On-Call Repair Services Project:</b></p> <p>In general, the project consists of installing concrete sidewalks, curb and gutter, valley gutter, accessible curb ramps, driveways, and asphalt base repairs or overlays in the public right of way.</p>	<p>Construction on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue is underway.</p> <p><a href="https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project">https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project</a></p> <p>No work is scheduled at this time No work is scheduled at this time</p> <p>The meter upgrades are continuing across the Menlo Park Municipal Water service area. A door hanger will be placed on the customer's door after work has been completed.</p>	<p>Moderate impact due to sidewalk demolition on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.</p>
	<p><b>Owner:</b> City of Menlo Park</p> <p><b>City Project Engineer:</b> Jordan Chu (650) 330-6782</p> <p><b>City Engineering Inspector:</b> Holani Vaka (650) 330-6753</p> <p><b>Contractor:</b> Catos General Engineering (510) 397-2677</p>		



## Menlo Park Construction News Update January 7th, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
2	<p><b>Automated Meter Infrastructure (AMI) Project:</b></p> <p>The AMI project will upgrade all water meters for Menlo Park Municipal Water (MPMW) customers. These new meters will record and transmit accurate, hourly data in near real-time.</p> <p>For more information, visit <a href="http://menlopark.gov/ami">menlopark.gov/ami</a></p>	<p>No work is scheduled at this time</p> <p>The meter upgrades are continuing across the Menlo Park Municipal Water service area. A door hanger will be placed on the customer's door after work has been completed.</p>	<p>No traffic impact is expected.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.</p>
	<p><b>Owner:</b> City of Menlo Park</p> <p><b>City Project Engineer:</b> Scott Jaw (650) 330-6694</p> <p><b>Contractor:</b> Concord Utility Services Garry Pesavento – Project Manager (951) 757-2597</p>		
