




CITY OF MENLO PARK

Not all projects are listed, for more information please reach out to Menlo Park Public Works (Publicworks@menlopark.gov, (650) 330-6740) for more information. **To return to the map please click on the project number on the left column of the following pages**

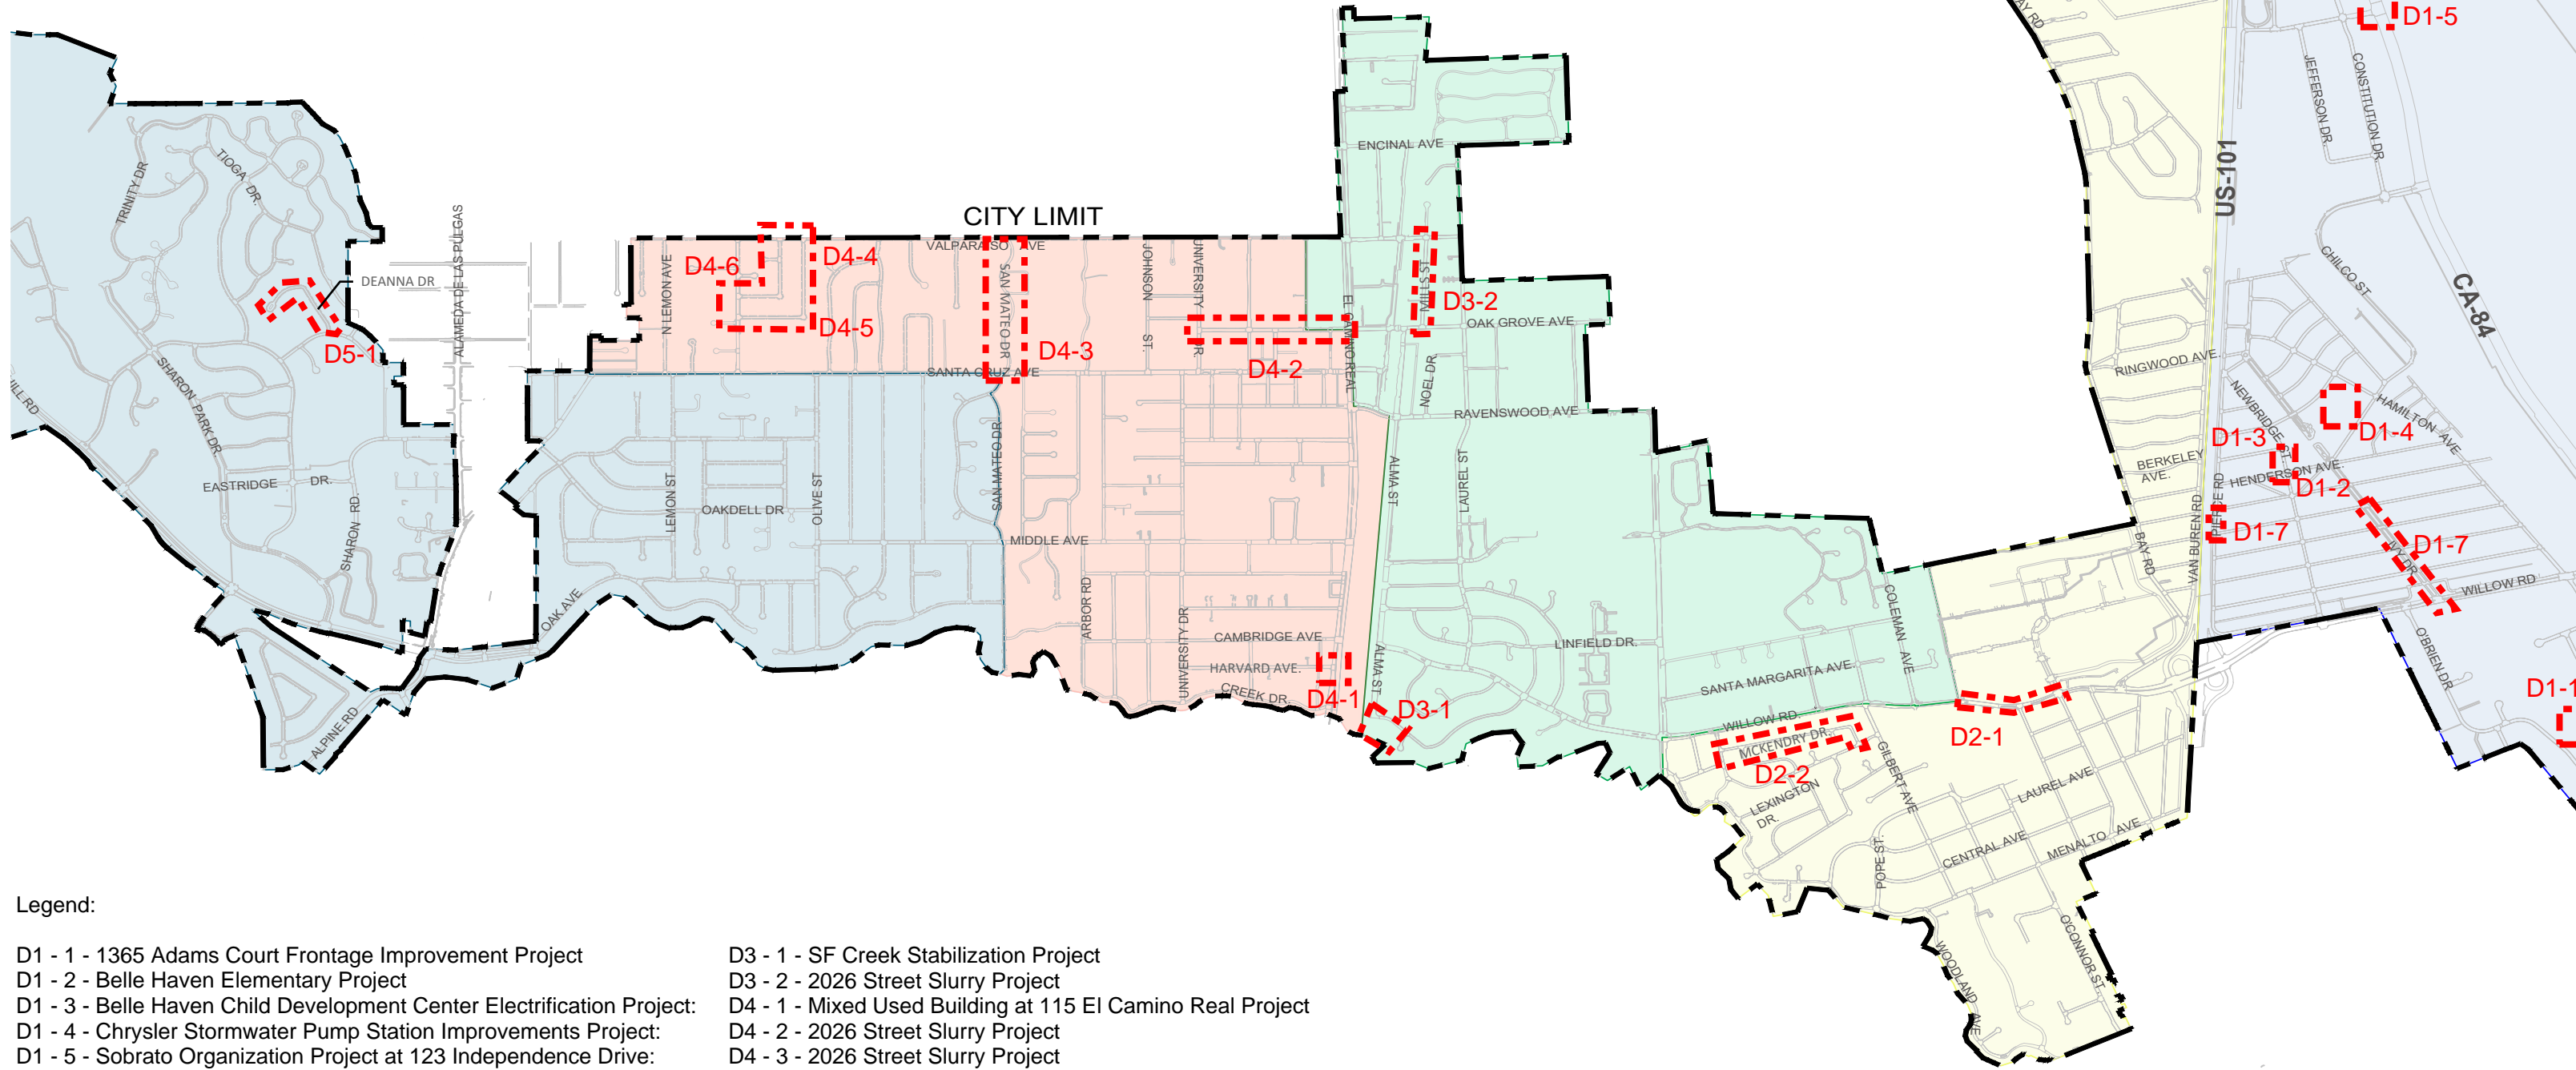

Legend:

- D1 - 1 - 1365 Adams Court Frontage Improvement Project
- D1 - 2 - Belle Haven Elementary Project
- D1 - 3 - Belle Haven Child Development Center Electrification Project:
- D1 - 4 - Chrysler Stormwater Pump Station Improvements Project:
- D1 - 5 - Sobrato Organization Project at 123 Independence Drive:
- D1 - 6 - Recycled Water Facilities Project
- D1 - 7 - Citywide Asphalt And Concrete On-Call Repair Services
- D1 - 8 - Moxy Hotel Project at 3723 Haven Avenue:
- D2 - 1 - Oak Gardens Veterans Housing Project
- D2 - 2 - 2026 Street Slurry Project

- D3 - 1 - SF Creek Stabilization Project
- D3 - 2 - 2026 Street Slurry Project
- D4 - 1 - Mixed Used Building at 115 El Camino Real Project
- D4 - 2 - 2026 Street Slurry Project
- D4 - 3 - 2026 Street Slurry Project
- D4 - 4 - West Bay Sanitary Point Repair Project
- D4 - 5 - Politzer & Hesketh Drive Water Main Replacement Project
- D4 - 6 - Streetlight High Voltage Circuit Replacement City of Menlo Park
- D5 - 1 - AT&T Utility Installation

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-1	<p>1365 Adams Court Frontage Improvement Project</p> <p>The works involving concrete ramp/sidewalk, crosswalk, streetlights, irrigation, landscape, stripping & other related improvements along Adams Drive and Adams Court.</p>	<p>Contractor is finalizing the remaining punch list items for permit signing.</p>	<p>Please anticipate traffic impacts including lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. Please anticipate traffic impacts including lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted. No anticipate traffic impacts.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: INTERTEK</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Eric Hinkley (650) 330-6749 Wilson Radford (650) 330-6742</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Davidovits/Valacad Co. Neal Gregorin General Superintendent (650) 218-1384</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-2	<p>Belle Haven Elementary Project</p> <p>The project is located at 415 Ivy Drive and involves the installation of concrete driveways, sidewalk, curb, & gutter along Chilco and Almanor Streets (City's ROW).</p>	<p>Contractor to schedule the pavement restoration along frontage. No construction schedule as of this time</p>	<p>Major traffic impacts due to lane closures.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, and flaggers as required) at all times during construction.</p>
	<p>Owner: Menlo Park School District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Wilson Radford (650) 330-6742</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Jacob Ciari, Project Engineer (408) 296-6010</p> <p>Start Date: 9/15/2025 Estimated date of completion: May 2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-3	<p>Belle Haven Child Development Center Electrification Project:</p> <p>The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.</p>	<p>The City is proceeding with the design phase. We are currently reviewing a Basis of Design document from KPA Group.</p>	<p>Major traffic impact is expected due to lane closure during operation.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City Of Menlo Park Project Manager: Matt Oscamou (650) 817-5292 Michael Fu (650) 330-6706</p> <p>City Of Menlo Park Project Inspector: Menlo Park Building Inspector</p> <p>Contractor: TBD</p> <p>Start Date: Spring 2026 End Date: Summer 2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**
Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-4	<p>Chrysler Stormwater Pump Station Improvements Project:</p> <p>The scope of work consists of furnishing & installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump & motor room, electrical control room, engine- generator room, pumping/electrical equipment & controls, hardscaping, landscaping, etc. to complete the work as per City approved plans & specs,</p>	<p>The contractor is working on the roof structure for the new pump station and finalizing the pump station software. Demolition of the existing pumps will commence once final testing of the new pumps is completed.</p> <p>Project completion anticipated for Summer 2026.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City Of Menlo Park Project Manager: Mitchell Supan (650) 330-6756</p> <p>City Of Menlo Park Project Inspector: Holani Vaka (650) 330 - 6753</p> <p>Contractor: APEC</p> <p>Start Date: May 2023 End Date: Summer 2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-5	<p>Sobrato Organization Project at 123 Independence Drive:</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives.</p> <p>Initial construction phase involves demolition and rough grading.</p>	<p>No site work activity is expected. Contractor to continue monitoring SWPPP and access to/from job site.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: Sobrato Organization</p> <p>City Of Menlo Park Project Manager: Edress Rangeen (650) 330-6712 Ebby Sohrabi (650)330-6743</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Sobrato Builders, Inc. Dino Spalding (Superintendent) (650) 695-1069</p> <p>Start Date: 05/30/2024</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-6	<p>Recycle Water Facilities Project</p> <p>The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process)</p>	<p>Contractor is scheduled to undertakes micro tunneling operation from jacking pit at Bayfront Park entry (Cargill property) to Independence Drive (City's ROW). Contractor to continues monitor and maintain the installed perimeter fence, traffic control plans, and dewatering system for the project.</p>	<p>Major traffic impact due to road closure at Independence/Constitution Drives starting 4/27 for an estimated 9 weeks duration. Minor traffic impact due to temporary pedestrian path adjustment at Bedwell Bayfront Park entry/exit area.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>
	<p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Ebby Sohrabi (650)330-6743 Eric Hinkley (650) 330-6749</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Anderson Pacific</p> <p>Start Date: 10/30/2024 End Revised Date:</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**
Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-7	<p>Citywide Asphalt And Concrete On-Call Repair Services Project:</p> <p>In general, the project consists of installing concrete sidewalks, curb and gutter, valley gutter, accessible curb ramps, driveways, and asphalt base repairs or overlays in the public right of way.</p>	<p>Public Works will be performing asphalt work on Pierce Road and Newbridge Street in the coming weeks in preparation for the upcoming Bay and Pierce Roads Improvement Project this summer.</p> <p>On Pierce Road, asphalt resurfacing will take place between Henderson and Windermere Avenue from April 28-29.</p> <p>on Newbridge Street asphalt repairs will occur between Windermere Avenue and Willow Road from April 30–May 1.</p>	<p>Pierce Road Work (Full Closure) From April 28–29, asphalt resurfacing will take place on Pierce Road between Henderson and Windermere Avenue.</p> <ul style="list-style-type: none"> The road will be closed to public traffic from 8:00 AM to 5:00 PM each day. Traffic will be detoured to Newbridge Street. <p>Traffic control measures will be in place to ensure public safety.</p> <p>Newbridge Street Work (Partial Closures) From April 30–May 1, asphalt repairs will occur on Newbridge Street between Windermere Avenue and Willow Road.</p> <ul style="list-style-type: none"> Please expect partial lane closures and traffic delays from 8:00 AM to 5:00 PM. <p>Traffic control will be in place to guide vehicles safely through the work area.</p> <p>Additional Information</p> <ul style="list-style-type: none"> Roadways will reopen to traffic at the end of each workday. Access to driveways will be maintained at all times. <p>Residents are encouraged to park outside of the work zones during construction hours.</p>
	<p>Owner: City of Menlo Park</p> <p>City Project Engineer: Mitchell Supan</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Catos General Engineering (510) 397-2677</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-8	<p>Moxy Hotel Project at 3723 Haven Avenue:</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, fencing, etc. on property. Initial construction phase involves demolition and rough grading.</p>	<p>Contractor is schedule to continue rough grading works On-site as part of the issued demolition permit. Contractor to continue monitoring SWPPP and access to/from job site.</p>	<p>Minor traffic impact expected during operation – truck/equipment exit/entering the site.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>City Of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: VCC USA Chris Martorana (Sr. Superintendent) (626) 392-3621</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-1	<p>Oak Gardens Veterans Housing Project:</p> <p>The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.</p>	<p>Contractor is scheduled to continue on-site building construction and off-site material deliveries using Willow Road.</p> <p>Contractor is scheduled to undertake punch list items for off-site improvements along Willow Road frontage (slurry sealing, stripping and landscape) prior to building occupancy.</p>	<p>Minor traffic impact due to lane closure/adjustment during operation along Willow Road.</p> <p>Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p>Owner: United State of America Department of Veterans Affairs (VA)</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: Guzman Construction Group (669) 224-9000</p> <p>Start Date: 12/12/2024 End Date: 02/02/2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-2 D3-2 D4-2 D4-3	<p>2026 Street Slurry Project</p> <p>The Project includes the base bid and bid alternate streets totaling 3.2 miles to maintain the City's overall PCI in good condition upon completion. The work generally includes: asphalt patching, crack sealing, and tree root remediation; slurry seal for base bid streets; grind (asphalt mill) and overlay for bid alternate streets; minor concrete work (e.g. broken gutter repairs and curb ramps at select locations); signing and striping; high visibility crosswalks for intersections located near schools; replacement of existing speed humps; and red curbs at select intersections per California's Daylighting Law (Assembly Bill 413).</p> <p>Owner: City of Menlo Park</p> <p>City of Menlo Park Project Manager: Andrea Mosqueda (650) 330 -6735</p> <p>City of Menlo Park Project Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: VSS International</p> <p>Start Date: Spring 2026 End Date: Summer 2026</p>	<p>The contractor is expected to begin minor concrete work on the week of 4/20. Dig-out repairs will begin the week of 4/27. The streets in bold will be the affected streets.</p> <p>Streets to receive slurry:</p> <ul style="list-style-type: none"> - Almanor Avenue - Windermere Avenue - Chester Street - McKendry Drive - O'Keefe Street - Gloria Circle - Mills Street - Oak Grove Avenue - San Mateo Drive - Garden Lane - Oak Hollow Way <p>Streets to receive grind and overlay:</p> <ul style="list-style-type: none"> - Mills Court - Poppy Avenue - Magnolia Street 	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-1	<p>San Francisquito Creek Bank Stabilization Project</p> <p>The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season</p>	<p>Caltrain is currently bidding the project. Construction is expected to continue in Spring 2026.</p>	<p>No major traffic impacts are expected at this time.</p>
	<p>Owner: Peninsula Corridor Joint Powers Board</p> <p>City Project Engineer: Mitchell Supan (650)330-6756</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Caltrans</p> <p>Start Date: Spring 2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-1	<p>Mixed Used Building at 115 El Camino Real Project</p> <p>This project consists of building a Mixed Used structure at the corner of El Camino Real and Harvard Avenue.</p>	<p>Contractor is scheduled to continue on-site construction.</p> <p>Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter).</p> <p>Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue.</p>	<p>Occasional minor traffic disturbances due to hauling, handling and material deliveries.</p> <p>Contractors shall provide traffic control approved by City as needed.</p>
	<p>City Project Engineer: Rambod Hakhamaneshi (650) 330-6759</p> <p>City Engineering Inspector: Wilson Radford (650) 330-6742</p> <p>Contractor: Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077</p> <p>Start Date: 03/04/2020 End Date: 12/15/2025</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**
Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-4	<p>West Bay Sanitary Point Repair Project</p> <p>The scope of work includes trenching to access the existing sewer mains, removal and replacement of existing sewer mains, and the subsequent restoration of all affected surfaces</p>	<p>Contractor will continue restoration work on the following streets:</p> <p>Politzer Dr. Hesketh Dr. Rosefield Wy. Hobart St. Cotton St. Hillview St.</p> <p>Schedule of construction activities is being communicated with the City to obtain accurate updates of the project.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector George Sanchez (650) 477 - 6425</p> <p>City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6741</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-5	<p>Politzer & Hesketh Drive Water Main Replacement Project</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Politzer & Hesketh Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Restoration and paving at Hesketh Dr. Is completed.</p> <p>Scheduled to complete the slurry overlaying at Politzer Dr. in May 2026.</p> <p>Schedule of construction activities is being communicated with the City to obtain accurate updates of the project.</p>	<p>Please anticipate major traffic impacts along Valparaiso Ave with surrounding , including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: California Water Service</p> <p>Cal Water Service Project Manager Andrew Westbrook (650) 334-5920</p> <p>City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6741</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Construction John Healy (408) 371-5510</p> <p>Start Date: 06/18/2025 End Date: 05/2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-6	<p>Streetlight High Voltage Circuit Replacement City of Menlo Park</p> <p>The project generally includes replacing existing high voltage electrical circuits with new conduits, conductors, and pull-boxes in the West Menlo neighborhood. The project will also replace existing luminaires with energy efficient LED luminaires and install new street poles and fixtures at select locations. Please refer to the project webpage for additional information including a map detailing proposed street location.</p>	<p>Contractor is scheduled to install light fixtures in the middle of May. After electrical will be installed through conduits to finalize installation</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations</p>
	<p>Owner: City of Menlo Park City of Menlo Park Project</p> <p>Manager: Holani Vaka (650) 330-6753</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Bay Area Lightworks</p> <p>Start Date: 10/13/2025 End Date: 07/31/2026</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-1	<p>AT&T Project along Dianne Drive. Work includes the installation of interduct telecommunications cables along Deanne Drive by means of open trenching, horizontal boring vis pits, restoration works along Deanne Drive fronting Lots nos.1005, 1055, 1045, 1035, 1025, 1075, 1060, 1095, 1130 in the public right of way.</p>	<p>Contractor is expected to undertake asphalt pavement restoration on affected areas at installed interduct communication cables along Deanne and Avy Avenue weather permit.</p>	<p>Please anticipate minor traffic impacts, including partial lane closures, during construction activity (typically 9AM – 3PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, and flaggers as required) at all times during operations.</p>
	<p>Owner: AT&T</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Haleigh Boss (408) 442-2712 Juan (650) 464-9908</p>		

Menlo Park Construction News Update April 29th, 2026

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
1	<p>Smart Irrigation Infrastructure Project</p> <p>Project involves upgrading of irrigation meters at 18 City facilities across the City. Work is being sequenced with first four sites being Burgess Park, Nealon Park, Jack W Lyle Park, and Kelly Park.</p> <hr/> <p>Owner: City of Menlo Park</p> <p>City of Menlo Park Project Manager: Ryan Bernal (650) 330-6713</p> <p>City Engineering Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: Medallion Landscape Ian Scott (408) 763-1902</p>	<p>Contractor has begun site preparation and equipment procurement for first five installations at the four sites. Will coordinate access and service interruptions with Public Works and Parks and Recreation Departments on as needed basis. Only minor and short term interruptions for access and irrigation are anticipated.</p>	<p>No traffic impact is expected.</p>
